

CMAQ PROJECT PLACERVILLE STATION II




Project Description

The project is located in the gravel lot adjacent to the existing Placerville Station (Mosquito Park and Ride) north of U.S. 50. The project includes:

- Construction of a 50-car parking lot with lighting and landscaping
- Bicycle racks and lockers
- Replacement of an existing water main and services
- Replacement of sewer connection
- Paving Mosquito Road between the westbound U.S. 50 off-ramp and Clay Street
- Realigning the existing segment of the El Dorado Trail
- Improved connection to El Dorado Transit and Amtrak Bus Service

Current Project Status

EDCTC programmed \$645,000 in CMAQ funds to the project in March of 2019. The utility relocation agreement with PG&E was approved at the December 10, 2019 Placerville City Council meeting.

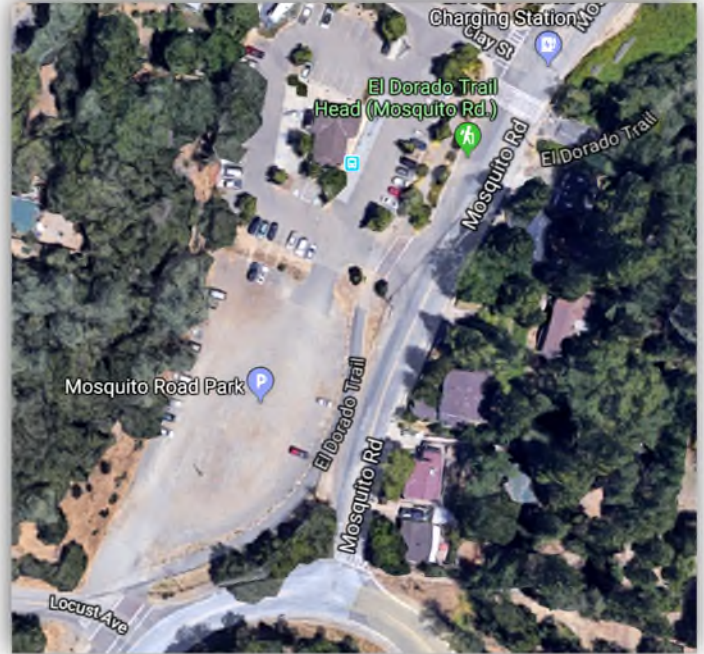

Upcoming Activities

- Permission to release for public bidding August 25, 2020
- Open Bids October 1, 2020
- Begin construction late fall 2020

PROJECT FUNDING DETAIL				
Project Phase	Amount Programmed	Source	Status	Project Cost
PA&ED / PS&E	\$200,000	FTA-5309 (c) - Bus	Obligated	\$200,000
ROW	\$10,000	Local	Programmed	\$10,000
Construction	\$645,000	CMAQ	Programmed	\$645,000
Construction	\$790,000	FTA-5309 (c) - Bus	Programmed	\$790,000
TOTAL	\$1,645,000			\$1,645,000
